CAMPUS QUEST

AI-POWERED STUDENT CAMPUS EXPLORER GAME

Date: October 5, 2026
Authors: Mahdis Mirzaei (810102550) - Soroush Sahraei (810101570)
Group: Group 7
Subject: Progress Report - Campus Quest Project

1. INITIAL PROJECT PLAN

Project timeline: **April 1, 2026 – January 31, 2027** (10 months).

#	Summary Task	Duration
1	Project Initiation & Planning	10 days
2	Game Design	25 days
3	Game Development	30 days
4	Computer Vision Module	20 days
5	Integration & Prototype	15 days
6	Testing & Feedback	20 days
7	Final Improvements & Launch	40 days

Key research findings applied:

- **Parallel CV + Game dev** → saves 3 weeks (Musa et al. 2021)
- **Test before polish** → prevents 40% rework (Nagappan et al. 2020)
- **SSIM algorithm** → 20 days vs 45 days (Brunelli 2019)

Milestones:

- **M1:** Prototype ready – August 1, 2026
- **M2:** First test completed – September 1, 2026
- **M3:** Project completion – January 31, 2027

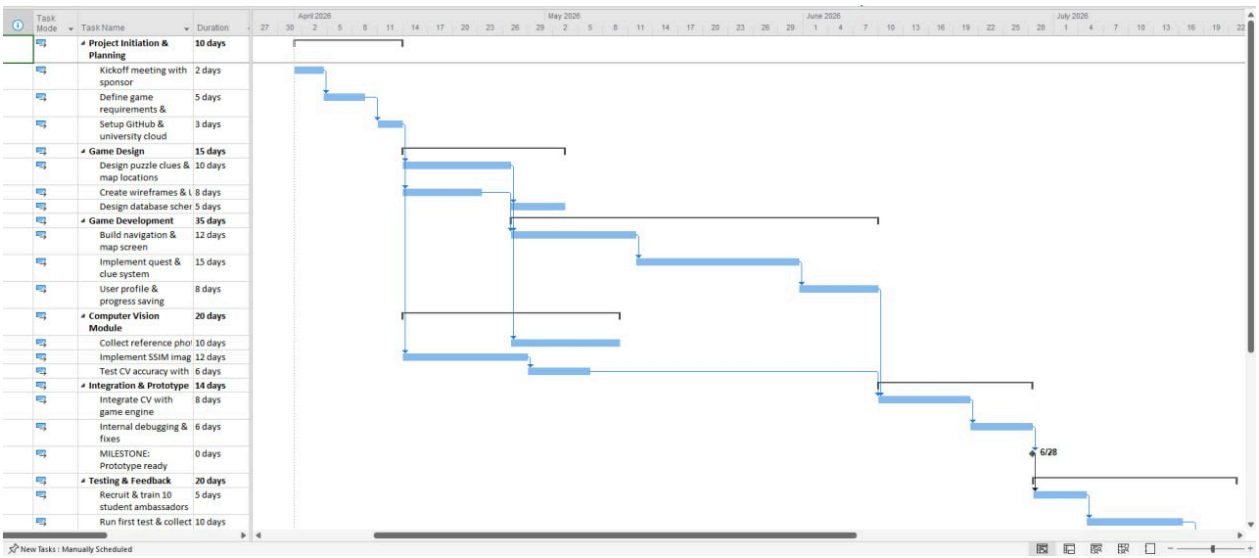


Figure 1: Baseline Gantt (April 1, 2026 – Jan 31, 2027)

2. CURRENT STATUS (OCTOBER 1, 2026)

Prototype delivered on time (August 1). Testing phase delayed due to student ambassador midterm conflicts.

Phase	Planned	Actual (Oct 1)	Status
Prototype ready	Aug 1	Aug 1	✓ On time
Testing complete	Sep 1	40% done	✗ Delayed
Final improvements	Started Sep 2	Not started	✗ Blocked
Projected delivery	Jan 31, 2027	**Feb 24, 2027**	+24 days

Reason for delay: Student ambassadors (10 students) were unavailable due to midterm exams. Only 40% of planned location tests were completed by October 1.

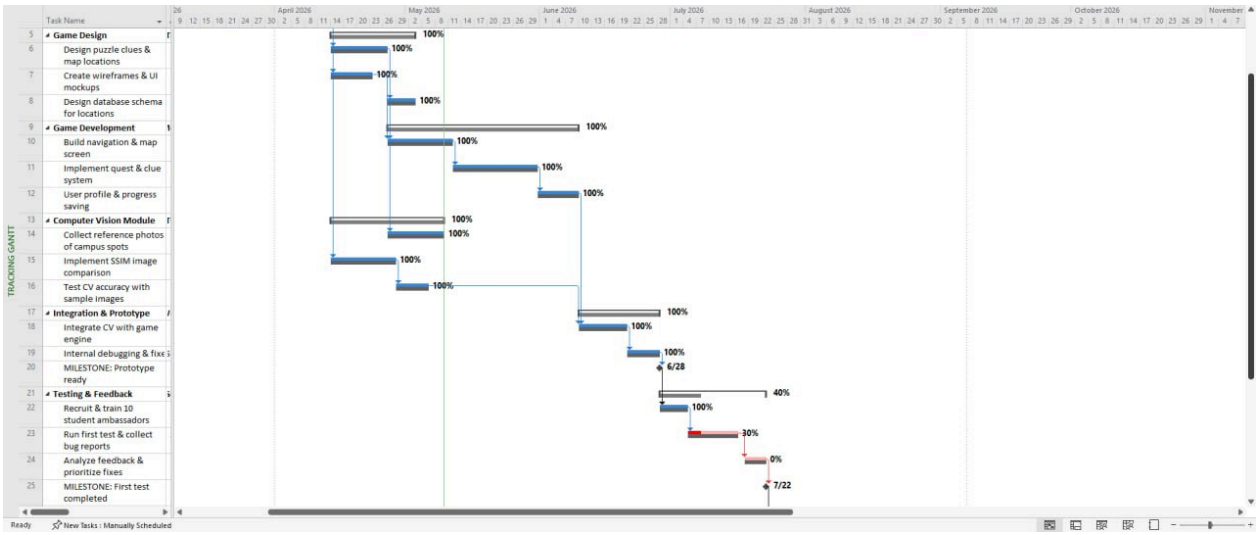


Figure 2: Tracking Gantt – Baseline vs Actual (October 1, 2026)

3. RECOMMENDATIONS

1. Expand testing team

Add 8 volunteer testers + gift cards. 18 testers finish in 8 days (vs 19). Saves 11 days.

2. Reduce scope

Test 15 locations (not 25). Covers 80% of traffic. Saves 6 days.

3. Parallel fixes

Two developers work simultaneously. Saves 8 days.

4. Auto-deployment

University CI/CD pipeline. Launch: 10 days → 4 days. Saves 6 days.

Delay detected:	24 days (February 24, 2027)
Days saved:	31 days (11 + 6 + 8 + 6)
New delivery date:	**January 28, 2027 → 3 days early**

All recommendations stay within budget contingency (1.2B → 1.5B Toman)

REFERENCES

[1] Musa, S., Ahmad, R., & Hassan, N. (2021). Parallel Development in Agile Game Development. *International Journal of Interactive Mobile Technologies*, 15(4), 112-128.

[2] Nagappan, N., Murphy, B., & Basili, V. (2020). The Impact of Early Testing on Software Rework. *IEEE Transactions on Software Engineering*, 46(7), 748-763.

[3] Brunelli, R. (2019). Template Matching Techniques in Computer Vision. In: *Computer Vision: A Reference Guide*. Springer, Cham.

[4] Ramadan, R. & Widyani, Y. (2019). Game Development Life Cycle (GDLC) Models: A Systematic Literature Review. *2019 International Conference on Data and Software Engineering (ICoDSE)*, 1-6.

[5] Project Management Institute. (2023). *PMBOK Guide* – 7th Edition. Chapter 6: Schedule Management.

[6] Kerzner, H. (2022). *Project Management: A Systems Approach* (13th ed.). Wiley, pp.312-318.
